

Longwood Central School District
Capital Improvement Project
Progress Report
August 2018

**PARK EAST
CONSTRUCTION
CORP.**



Capital Bond Projects:

Current

Junior HS

- ▶ Roof Replacement
- ▶ Masonry Reconstruction
- ▶ Track Reconstruction
- ▶ Asphalt Paving
- ▶ Replace Track

Senior HS

- ▶ Asphalt Paving
- ▶ Replace Tennis Courts
- ▶ New Multipurpose Turf Field
- ▶ Softball & Baseball Turf Infields
- ▶ Masonry Reconstruction Phase II

Upcoming

Maintenance Garage
Playgrounds



Longwood Central School District

General Bond Status Update
Junior HS Roof Replacement
August 2018 Progress Report

Junior HS

Current Projects:



Project	Start	Finish	%Complete
Roof Replacement	June 26 th 2018	September 31st 2018	70%



Longwood Junior HS



Current Projects:

Project	Start	Finish	% Complete
Asphalt Paving	June 2018	August 2018	98%
Replace Track	June 2018	September 2018	75%
Replace Sidewalks & Curbs	June 2018	August 2018	98%



JHS Track Paving



JHS Track Reconstruction



JHS Track Replacement



JHS Track Paving



JHS Track Paving



JHS Track Paving



JHS Flat Work



JHS Roof Replacement



Longwood Senior HS

Current Projects:



Project	Start	Finish	%Complete
Asphalt Paving	August 2018	August 2018	100%
Replace Tennis Courts	June 2018	September 2018	75%
Multipurpose Field	June 2018	September 2018	75%
Replace Sidewalks and Curbs	August 2018	August 2018	100%
Baseball & Softball Turf Infields	August 2018	September 2018	40%



HS Track Recoating



HS Track Recoating



Multipurpose Field Under Turf
Drainage



HS Parking Lot Paving



Multipurpose Final Stone Layer



HS Multipurpose Field



HS Parking Lot Paving



HS Tennis Court




Multipurpose Field Retaining Wall And Fence



Multipurpose Field Curb and Fence



HS Multipurpose Field
Ready for New Turf

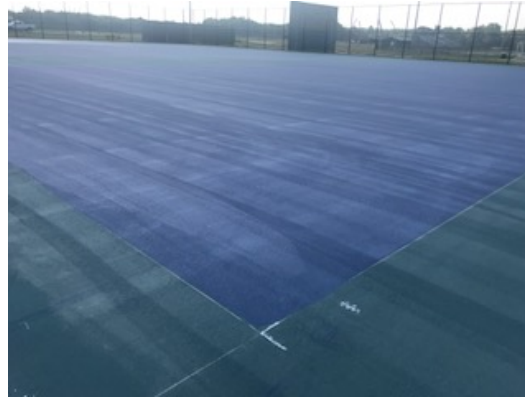

HS Tennis Courts



HS Tennis Courts



Multipurpose Field Retaining
Wall And Fence

Longwood Central
School District
August 2018 Update

**PARK EAST
CONSTRUCTION CORP.**
